


# SWMP UPDATE



# WATER DEMANDS & RETURNS

- Report complete
- ACFS reviews complete
- Agency reviews complete
- Awaiting acceptance

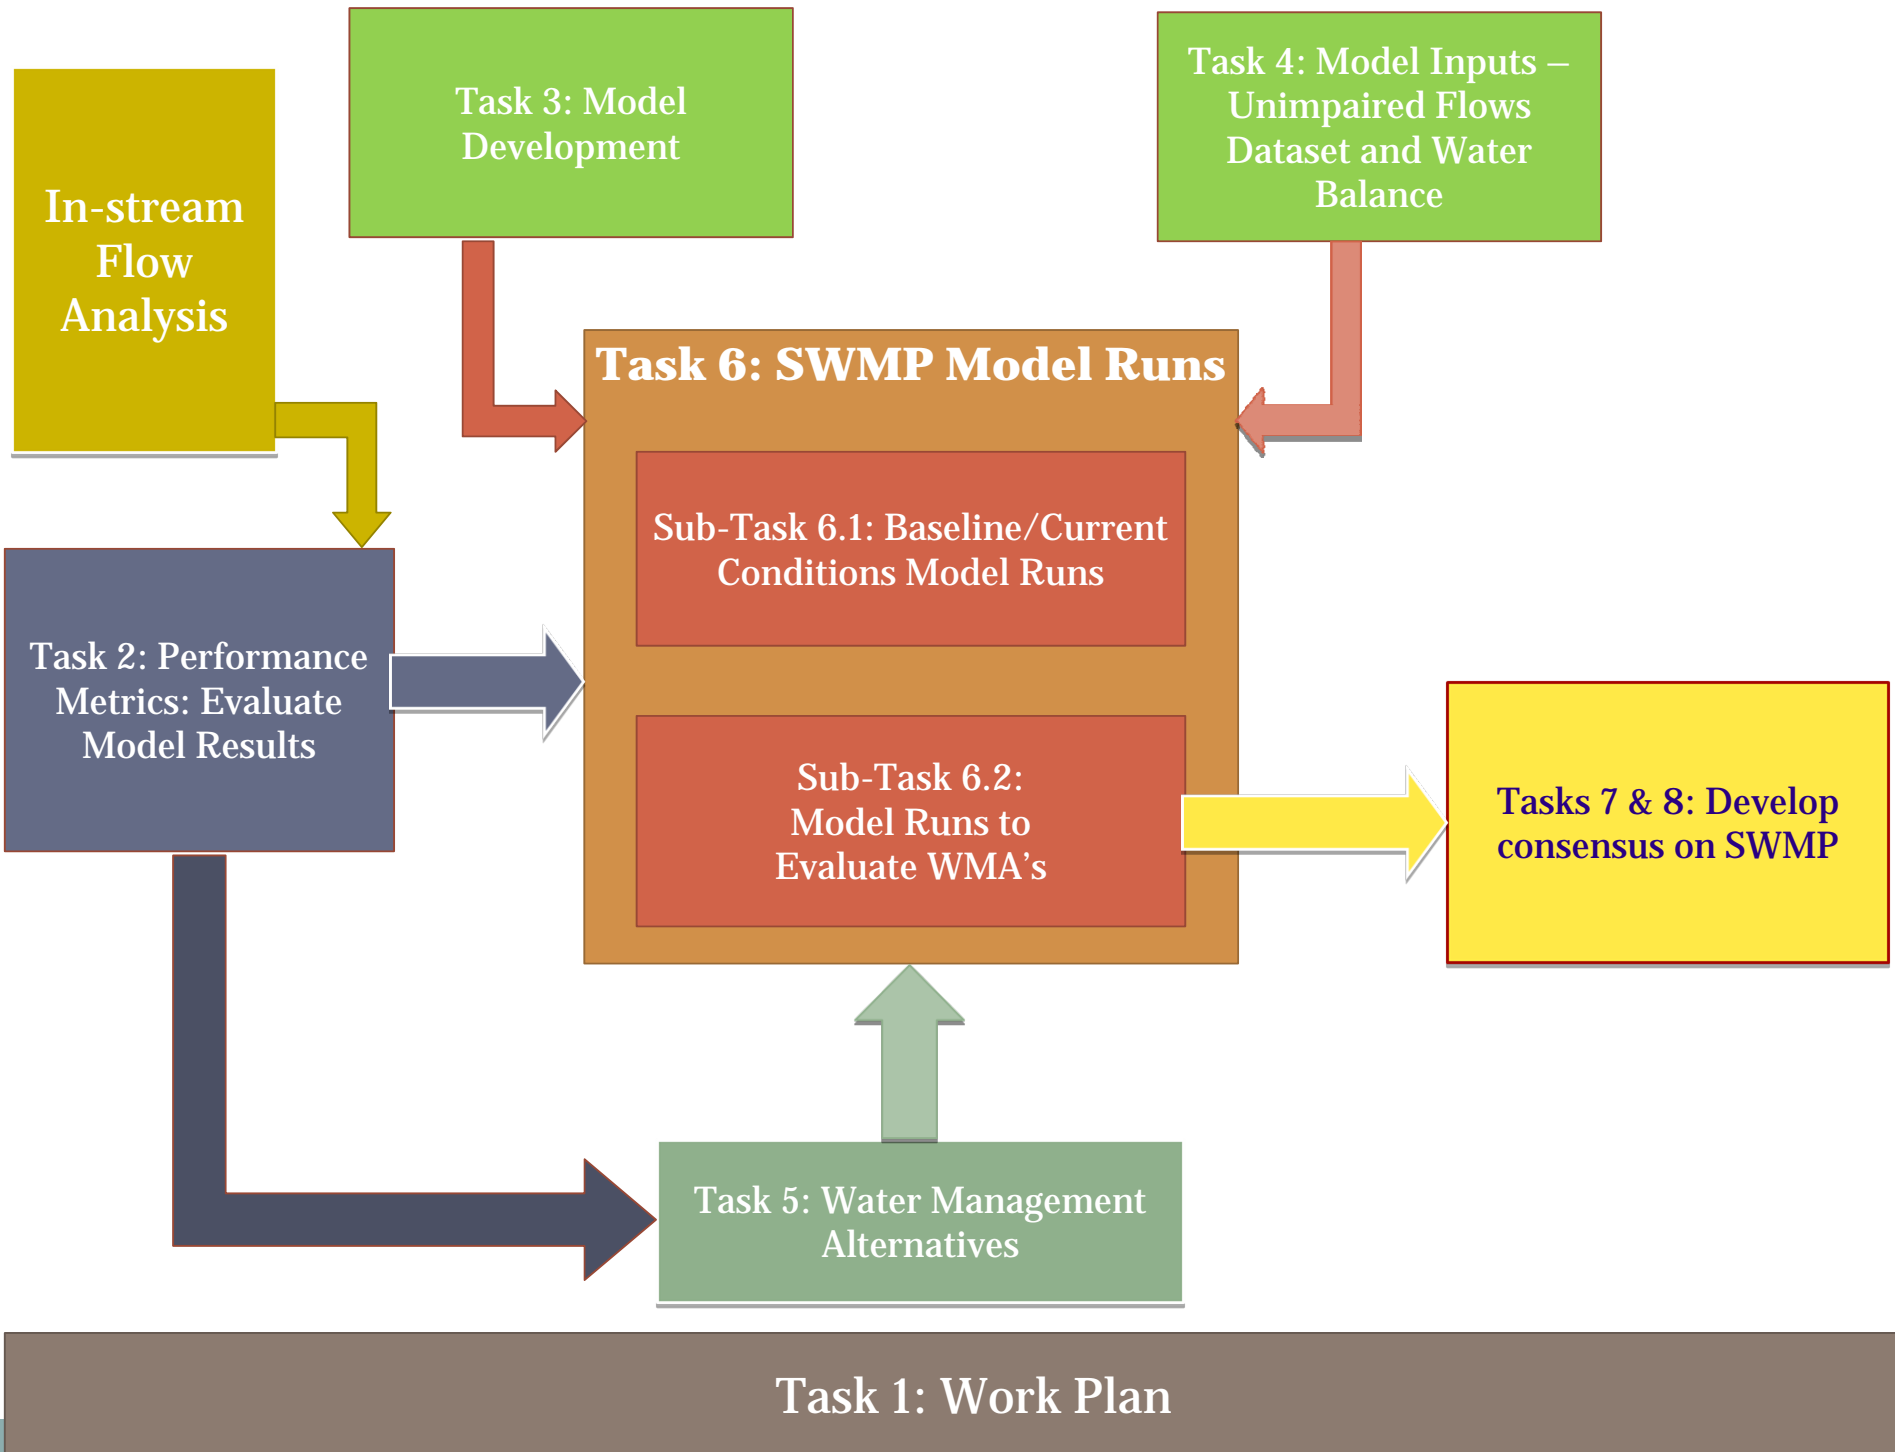

# UNIMPAIRED FLOWS

- GWRI report complete
- Decision to use current USACE data set



# IFA & ENVIRONMENTAL

- IFA report complete
- Environmental interest group reviewing
- Gordon to provide additional information



# PERFORMANCE METRICS

- Causus meetings complete
- Still getting interest group input
- Existing conditions model runs used latest metrics
- Needs GB acceptance



# EXISTING CONDITIONS MODEL RUNS

- Runs complete
- B&V and GWRI to present results today
- Needs GB acceptance



# WATER MANAGEMENT ALTERNATIVES

- COMPLETED CAUCUS  
INPUTS
- HAVE APPROXIMATELY  
40
- STILL ACCEPTING WMA  
INPUTS TILL MAY 10TH





# SCREENING WMA's

- Defining the process
- TOCWG to start initial screening in May



# ITERATIVE RUNS

- First of 3 run sets to start early July
- Each run to take approximately 6 weeks



# SCHEDULE



- On track to complete by April/May 2014

	Jan	Feb	Mar	Apr*	May	June*	July	Aug	Sept*	Oct	Nov	Dec*	Jan	Feb	Mar	Apr*	May*	June
<b>Phase A (Approved)</b>																		
Task 1: Detailed Work Plan																		
Task 4.1.1 IFA Literature Review																		
<b>Phase B (Approved by GB March 2012)</b>																		
Task 2: Prob Defn/Perf Indicators																		
Task 3.1: Model Set-Up <sup>2</sup>																		
Task 3.2 & 3.3: Model Tailoring <sup>2,3</sup>																		
Task 4.2: Unimpaired Flows <sup>3</sup>																		
Tasks 4.2-4.4 Water Demands/Report																		
Task 5.1: Water Mgmt Alt Template <sup>4</sup>																		
Task 4.1.2-4.1.3 Data/Science needs																		
Task 4.1.3.1, 4.1.3.2, & 4.1.4 Apal IFA																		
<b>Phase C (Approved by GB May 2012)</b>																		
Task 4.1.5: Conc IFAs (FI/Chatt)																		
Task 5.2: Solicit WMAs <sup>4</sup>																		
Task 5.3-5.4: Screen WMAs <sup>4</sup>																		
Task 6.1 Existing Conditions Modeling <sup>3,5</sup>																		
B&V - Phase C, caucus meetings Expert WMA Panel																		
<b>Phase D (Approved by GB Sept 2012)</b>																		
Task 6.1 Existing Conditions Modeling <sup>3,5</sup>																		
B&V - Phase D, caucus meetings																		
<b>Phase E (Approved by GB Dec 2012)</b>																		
Task 4.1.4 Estuary Assessment																		
Task 6.2: Iterative Modeling <sup>3,8</sup>																		
Support for Contractor Meeting Attendance <sup>9</sup>																		
<b>Future Phases and Tasks</b>																		
Task 6.2 (remainder): Iterative Modeling <sup>3,8</sup>																		
Task 7: Consensus Building <sup>8</sup>																		
Task 8: Draft plan/report																		
<b>SWMP Facilitation<sup>6</sup></b>																		
2013 (Bingham and Masters) -- Approved																		
2013 Bingham (July - December) <sup>10-</sup>																		

Phase B (Approved by GB March 2012)

Task 2: Prob Defn/Perf Indicators

Task 3.1: Model Set-Up<sup>2</sup>

Task 3.2 & 3.3: Model Tailoring<sup>2,3</sup>

Task 4.2: Unimpaired Flows<sup>3</sup>

Tasks 4.2-4.4 Water Demands/Report

Task 5.1: Water Mgmt Alt Template<sup>4</sup>

Task 4.1.2-4.1.3 Data/Science needs

Task 4.1.3.1, 4.1.3.2, & 4.1.4 Apal IFA

Phase C (Approved by GB May 2012)

Task 4.1.5: Conc IFAs (FI/Chatt)

Task 5.2: Solicit WMAs<sup>4</sup>

Task 5.3-5.4: Screen WMAs<sup>4</sup>

Task 6.1 Existing Conditions Modeling<sup>3,5</sup>

B&V - Phase C, caucus meetings

Expert WMA Panel

Phase D (Approved by GB Sept 2012)

Task 6.1 Existing Conditions Modeling<sup>3,5</sup>

B&V - Phase D, caucus meetings

Phase E (Approved by GB Dec 2012)

Task 4.1.4 Estuary Assessment

Task 6.2: Iterative Modeling<sup>3,8</sup>

Support for Contractor Meeting Attendance<sup>9</sup>

Future Phases and Tasks

Task 6.2 (remainder): Iterative Modeling<sup>3,8</sup>

Task 7: Consensus Building<sup>8</sup>

Task 8: Draft plan/report

SWMP Facilitation<sup>6</sup>

2013 (Bingham and Masters) -- Approved

2013 Bingham (July - December)<sup>10-</sup>

decision deferred

modifications requested

addl WMAs

to be determined  
.....

#1

#2

#3

# FACILITATION

- Proposed for Gail to now facilitate SWMP for TOCWG, EC and GB



# CURRENT PRIORITIES

- SWMP completion and input for WCM update
- Apalachicola Bay evaluation
- Funding



# USACE WCM UPDATE

- Spring 2013 – Summer 2014 **Alternative Development & Impact Analysis**
- May- June 2014 **Public Meetings on Analysis Results**
- Summer 2014 – Summer 2015 **Technical Review**
- Summer 2015 **Draft EIS with Public Comment**
- Spring 2016 **ROD Signed**
- Summer 2016 **Implement New WCM**

# PARKING LOT ISSUES

- Corrections to UIF
- Additional environmental study and monitoring
- Update demands data

